

CONSTRUCTION PROGRESS

This 14-month project has been under way for six months and approximately 30% of the project has been completed.

Contract C1036 for the rehabilitation of 12.78 km of MR240 (the R399) between Vredenburg and Paternoster has been divided into five sections of approximately 2.5 km each. The contractor is currently busy with rehabilitation works on three of the five sections.

POSSIBLE DELAYS

Weather

There have been no weather-related delays to date.

Materials

Material for these roadworks is sourced commercially and from cuttings. No delays are foreseen.

ROAD AND ACCESS CLOSURES

Three sections of road are closed to two-way traffic. Rehabilitation work is being done in half-widths, with stop/go controls enabling traffic to use the open lane. No accesses are closed.

GENERAL TRAFFIC ACCOMMODATION

The road has been temporarily widened to facilitate half-width construction. Although stop/go controls are in place on sections under construction, traffic volumes are relatively low, and no problems have been experienced.

INTERESTING FACTS

All labour requirements are sourced from Paternoster and Vredenburg. All materials are tested on site by the on-site soils laboratory.

CONTACT NUMBERS


General enquiries: 082 338 5566
Road emergencies: 082 219 3282

Traffic accommodation enquiries: 082 219 3282/084 654 0066
If you have any queries or complaints, please contact us. We want to ensure our construction zone is safe for road users and construction workers.

PROGRESS REPORT

REHABILITATION OF MR240 (R399) VREDENBURG TO PATERNOSTER

WORK COMPLETED

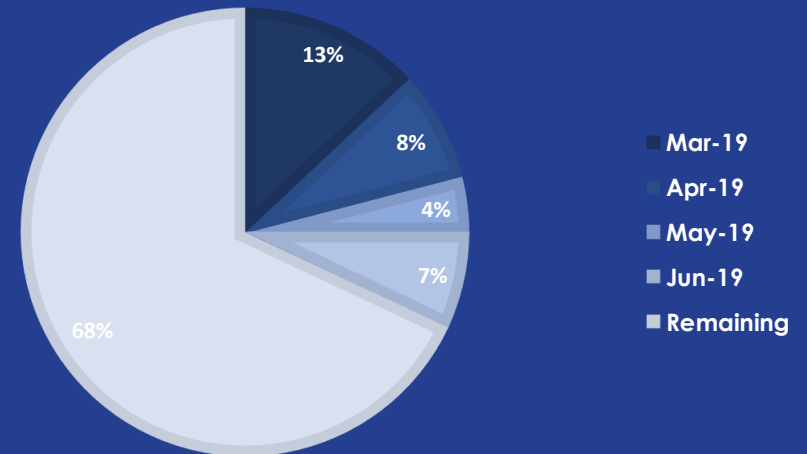

The Western Cape Government is working hard to maintain our roads. Please drive carefully during this period of construction. Let us work together to ensure that our roads are safe. **BETTER TOGETHER.**



Western Cape
Government

Transport and Public Works

BETTER TOGETHER.
